PROJECT PLANNING PHASE

Project Planning Template

Product Backlog • Sprint Planning • User Stories • Story Points

Metro Ticket Generating System in ServiceNow

Date	16 October 2026	**Maximum Marks**	5 Marks

1. Product Backlog, Sprint Schedule, and Estimation

The product backlog below translates the project scope into epics and user stories. Story points are relative effort estimates, and priorities indicate the proposed order of delivery. Team member assignments are left as role-based placeholders because individual names were not provided.

Sprint	Functional Requirement / Epic	User Story No.	User Story / Task	Story Points	Priority	Team Members
Sprint 1	Requirements & Setup	USN-1	As a project administrator, I can define the ticket information to be captured so that the ticket form meets the project requirements.	2	High	ServiceNow Developer
Sprint 1	Requirements & Setup	USN-2	As an authorized user, I can access the ticket application according to my assigned role so that access is controlled.	1	High	ServiceNow Developer
Sprint 1	Ticket Form & Data	USN-3	As a passenger or staff user, I can enter required journey and ticket details in a form so that a ticket request can be submitted.	3	High	ServiceNow Developer
Sprint 1	Ticket Form & Data	USN-4	As a user, I receive validation feedback when required ticket information is missing or invalid so that I can correct the form.	3	High	ServiceNow Developer
Sprint 1	Ticket Form & Data	USN-5	As the system, I can store submitted ticket information in a structured ServiceNow record so that it can be retrieved and managed.	3	High	ServiceNow Developer
Sprint 2	Ticket Generation	USN-6	As a user, I can submit valid ticket details and have a ticket record generated with a unique reference so that I can identify my request.	5	High	ServiceNow Developer
Sprint 2	Ticket Generation	USN-7	As the system, I can update the ticket status through configured workflow logic so that the request lifecycle is tracked.	4	High	ServiceNow Developer
Sprint 2	Confirmation & Administration	USN-8	As a user, I can see confirmation and my ticket reference after successful submission so that I know the request was recorded.	2	High	ServiceNow Developer
Sprint 2	Confirmation & Administration	USN-9	As authorized staff, I can review and update ticket records so that ticket requests can be managed.	2	Medium	ServiceNow Administrator
Sprint 2	Testing & Review	USN-10	As a project team member, I can test form validation, ticket creation, access permissions, and error cases so that key flows are checked.	5	High	Testing / Project Team
Sprint 2	Testing & Review	USN-11	As a project team member, I can resolve identified issues and prepare a demonstration so that the project can be reviewed.	2	Medium	Project Team
Total			**Planned backlog total**	**32**		

Story point scale

Points	Effort meaning
1	Very easy / small task
2	Normal / straightforward task
3	Moderate task
5	Difficult / more complex task

2. Project Tracker and Sprint Schedule

The following dates are proposed planning dates, not confirmed execution dates. Planned story points are taken from the backlog above. Completed points and actual release dates must be updated at the end of each sprint based on the team's actual results.

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date	Planned Story Points	Completed Points	Actual Release Date
Sprint 1	12	6 working days*	19 Oct 2026	24 Oct 2026	12	To be updated	To be updated
Sprint 2	20	6 working days*	26 Oct 2026	31 Oct 2026	20	To be updated	To be updated

*Sprint dates and duration are suggested for planning and should be adjusted to the team's calendar. The template does not provide actual completion or release data.

3. Velocity Calculation

Velocity is the number of story points completed in a sprint. The average velocity per sprint is calculated from completed points, not just the planned backlog.

Measure	Calculation / Status	Result
Planned total story points	Sprint 1: 12 + Sprint 2: 20	32 planned points
Average planned load	32 planned points ÷ 2 sprints	16 points per sprint
Actual average velocity	Total completed points ÷ number of completed sprints	To be calculated after sprint reviews

Important: 16 points per sprint is the average planned workload for this plan. It is not a verified team velocity until actual completed story points are recorded.

4. Burndown Chart

A burndown chart tracks the amount of work remaining over the sprint timeline. The team should update the remaining story points each working day. Since no daily completion history was provided, the chart below is a blank tracking template rather than a claim about actual progress.

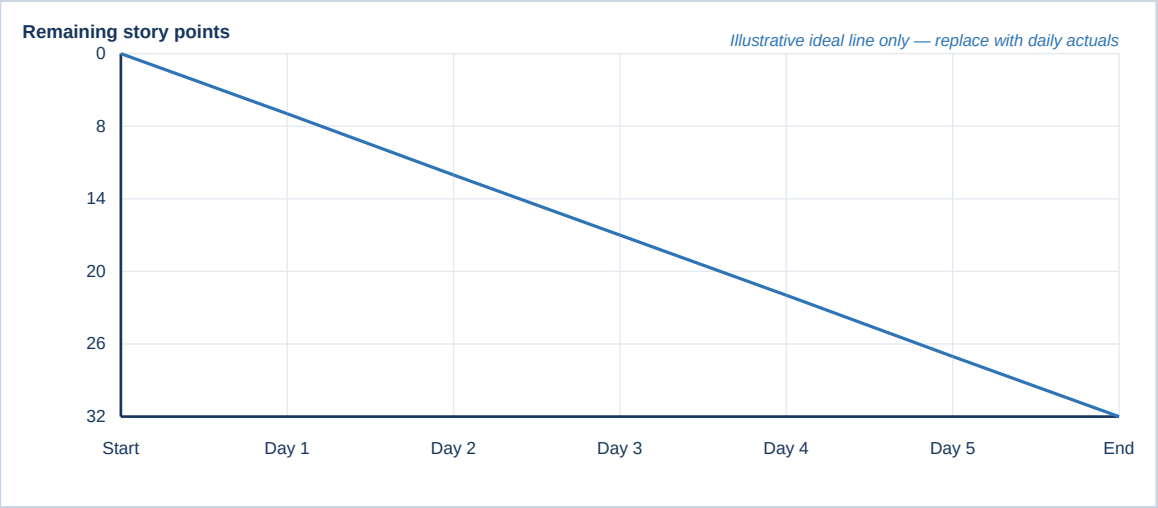

5. How to Maintain the Tracker

- At sprint planning, confirm stories, priorities, assigned team members, and story points.
- During the sprint, move work through the team's board according to its real status and record remaining points.
- At sprint review, record completed story points and the actual release date, if released.
- Recalculate average velocity using completed points from finished sprints, and use the result to inform future planning.

Scope note: The backlog is tailored to the Metro Ticket Generating System in ServiceNow. Integrations such as payment gateways, live metro APIs, and QR scanning are not included because they were not specified in the supplied project material.
